



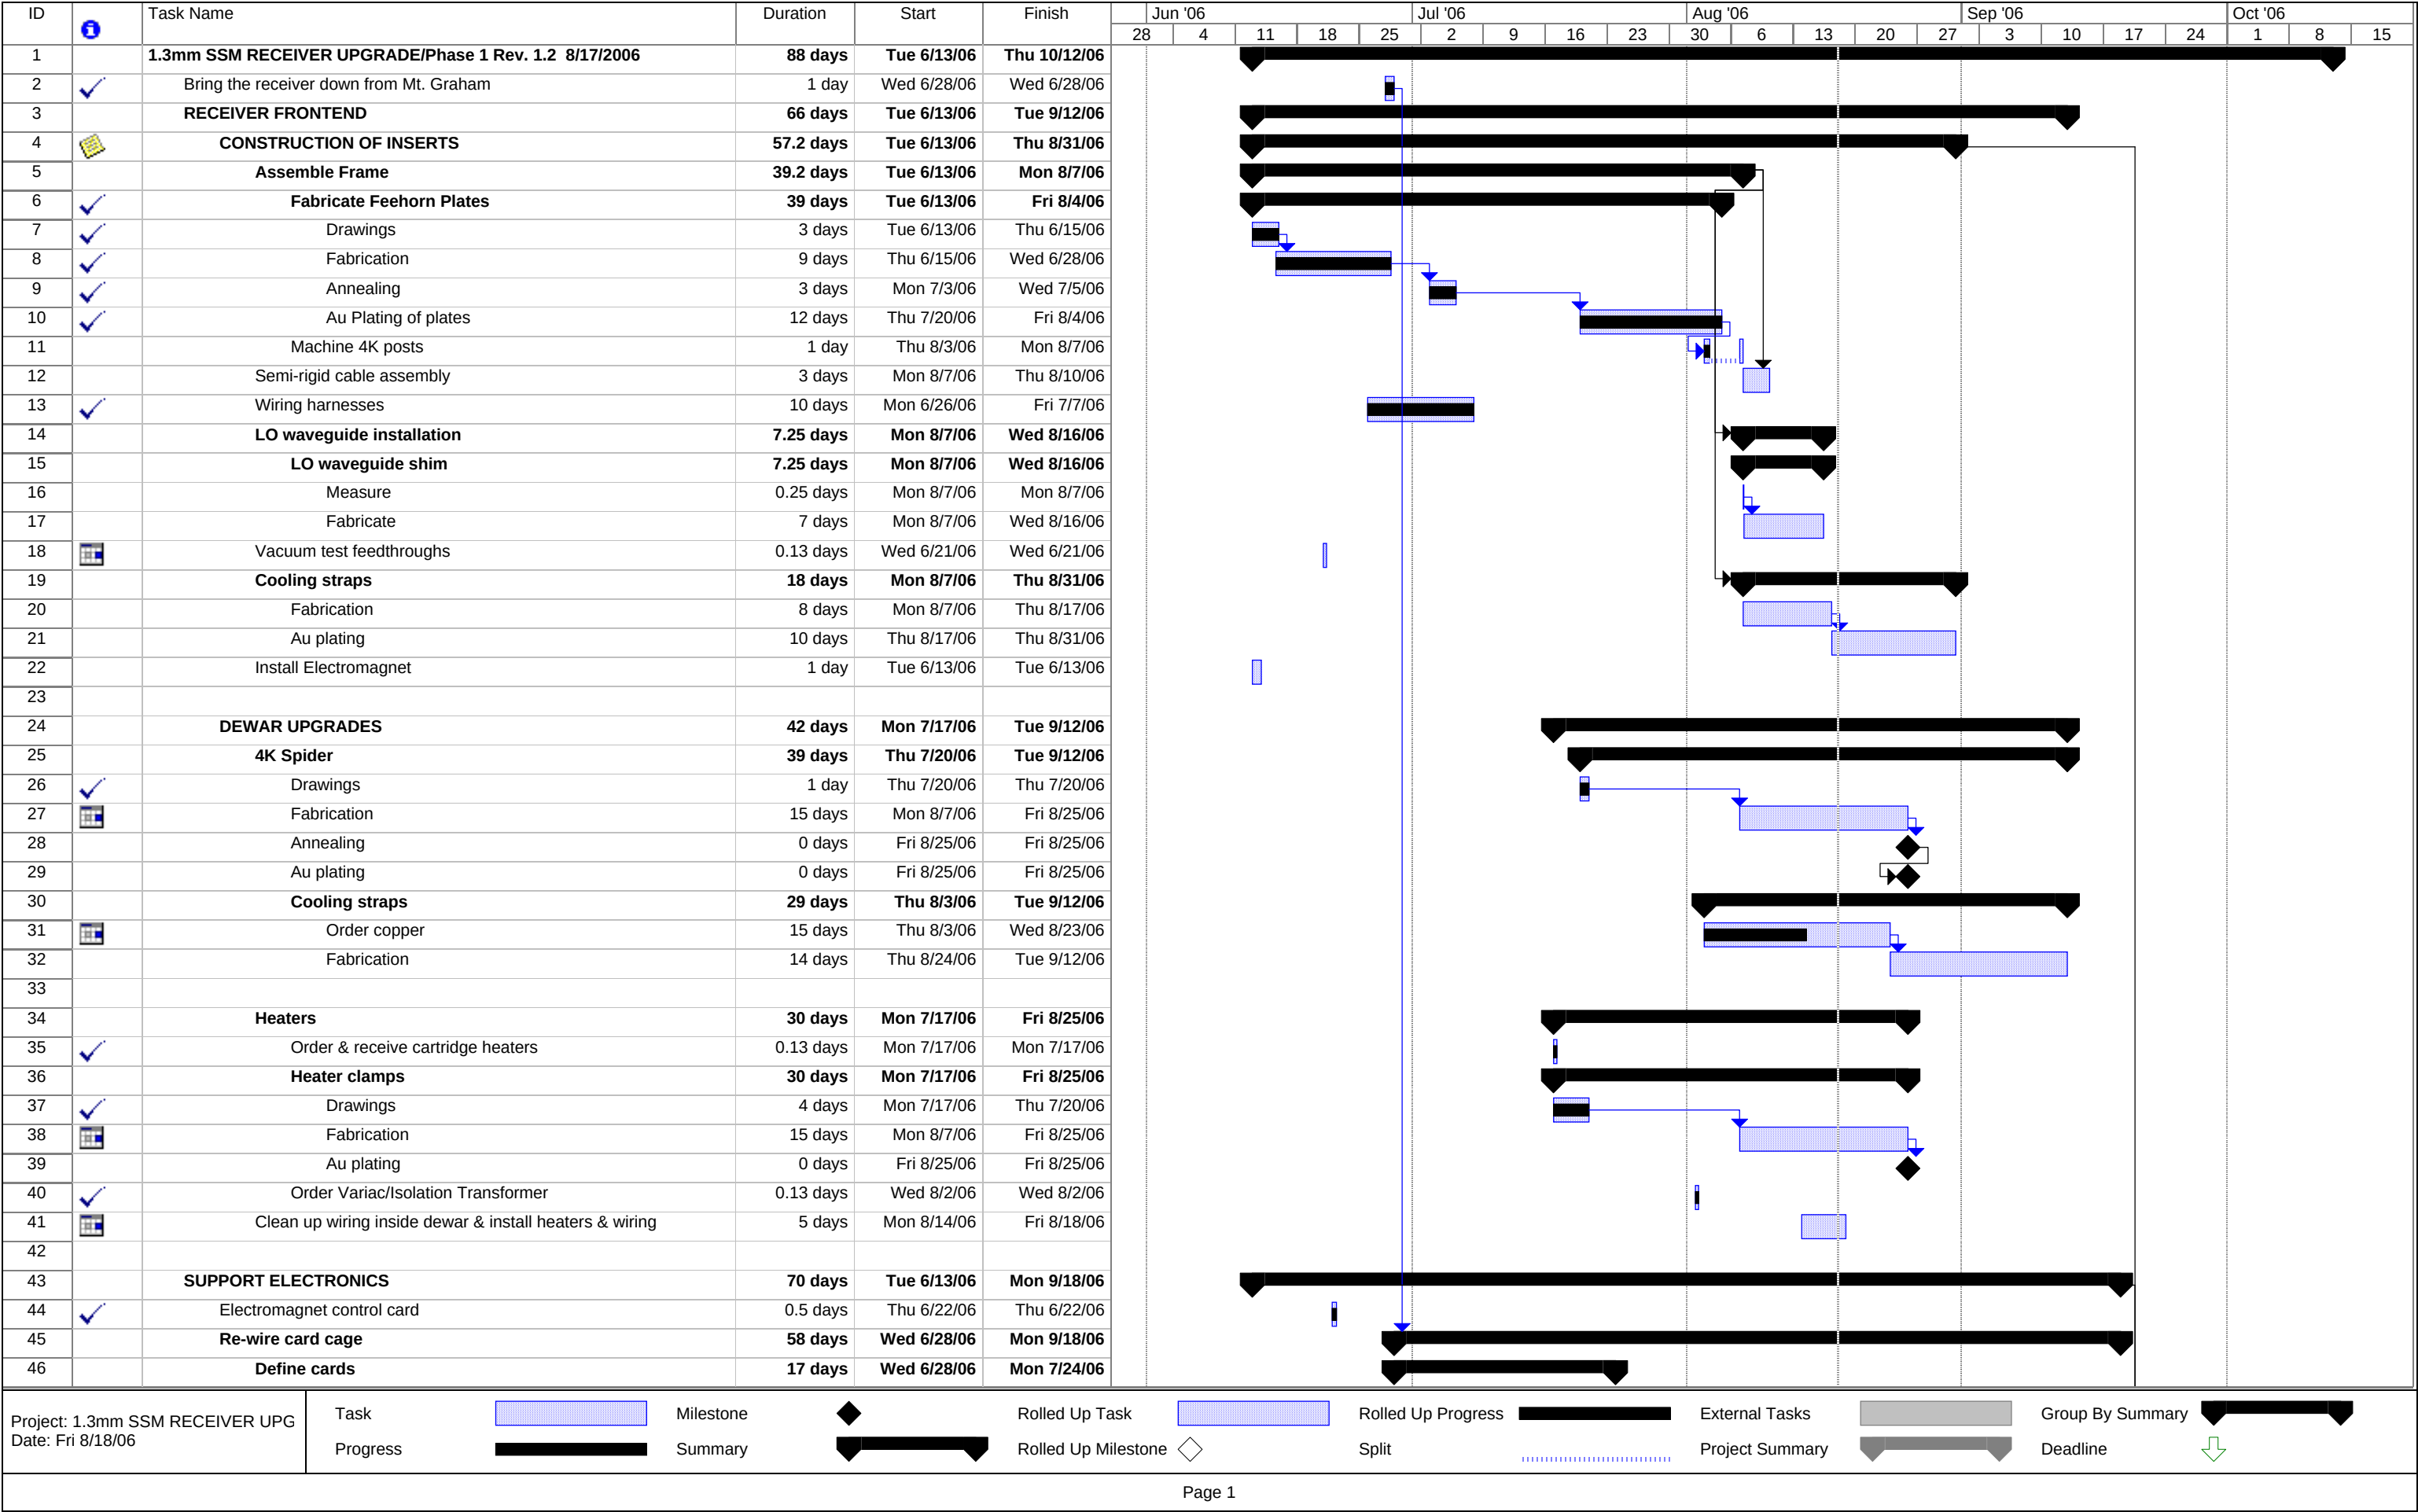

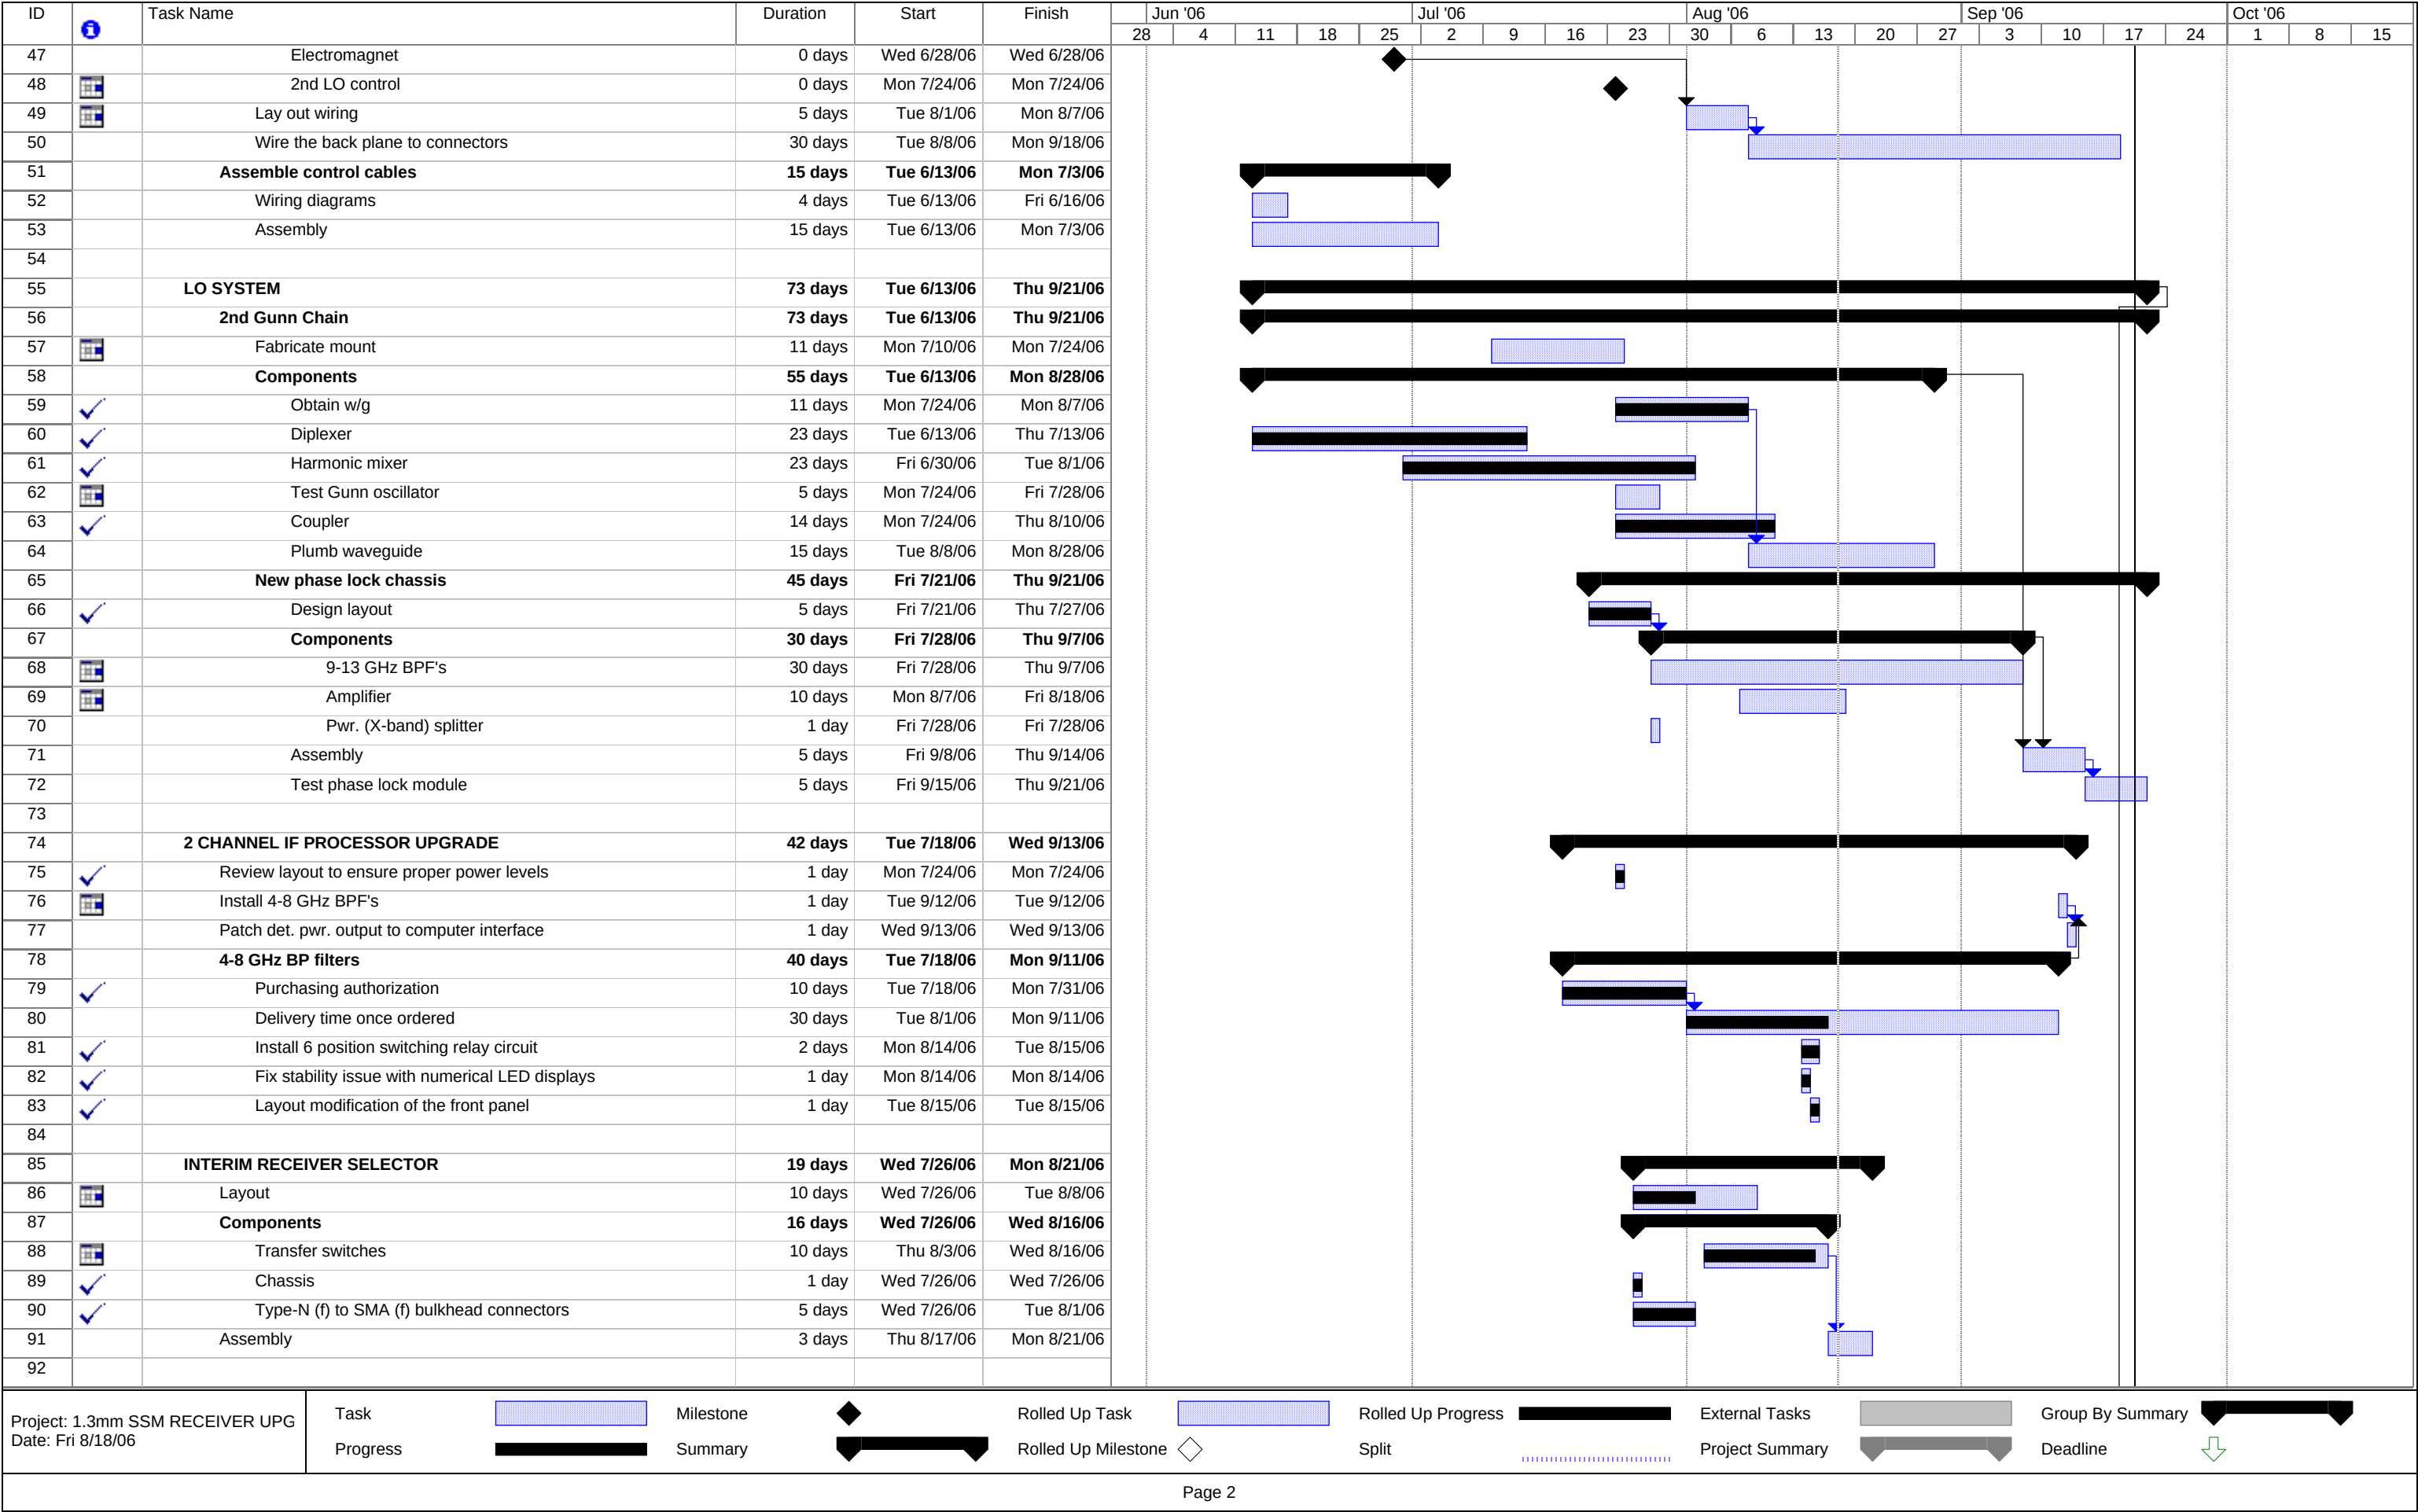

ID		Task Name	Duration	Start	Finish	Jun '06					Jul '06				Aug '06					Sep '06				Oct '06			
						28	4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	
93		IF CONVERTER SYSTEM	63 days	Wed 7/12/06	Fri 10/6/06																						
94		IF CONVERTERS	63 days	Wed 7/12/06	Fri 10/6/06																						
95		Plan layout	3.5 days	Mon 8/21/06	Thu 8/24/06																						
96		Converter crate	25 days	Mon 8/7/06	Fri 9/8/06																						
97		Design	5 days	Mon 8/7/06	Fri 8/11/06																						
98		Fabrication	20 days	Mon 8/14/06	Fri 9/8/06																						
99		Power supply/LO box	29 days	Mon 8/7/06	Thu 9/14/06																						
100		Power supply box design	3 days	Mon 8/7/06	Wed 8/9/06																						
101		LO box design	7 days	Wed 8/9/06	Thu 8/17/06																						
102		Fabrication	20 days	Fri 8/18/06	Thu 9/14/06																						
103		Components	63 days	Wed 7/12/06	Fri 10/6/06																						
104		4 - 8 GHz amplifiers	15 days	Wed 7/12/06	Tue 8/1/06																						
105		4 - 6 GHz output mixers	15 days	Wed 7/12/06	Tue 8/1/06																						
106		10. 4/1.3 GHz BPF's (Qty. 5)	40 days	Tue 7/18/06	Mon 9/11/06																						
107		Purchasing authorization	10 days	Tue 7/18/06	Mon 7/31/06																						
108		Delivery once ordered	30 days	Tue 8/1/06	Mon 9/11/06																						
109		15. 4GHz BPF's	40 days	Tue 7/18/06	Mon 9/11/06																						
110		Purchasing authorization	10 days	Tue 7/18/06	Mon 7/31/06																						
111		Delivery once ordered	30 days	Tue 8/1/06	Mon 9/11/06																						
112		IF controller ("Bud") board	26 days	Tue 8/1/06	Tue 9/5/06																						
113		PC board layout	11 days	Tue 8/1/06	Tue 8/15/06																						
114		Fabrication/assembly	15 days	Wed 8/16/06	Tue 9/5/06																						
115		100 MHz Phase lock source & pwr splitters	40 days	Mon 8/14/06	Fri 10/6/06																						
116		Power Splitters	5 days	Mon 8/7/06	Fri 8/11/06																						
117		15.4 GHz Oscillator (DRO)	45 days	Mon 7/24/06	Fri 9/22/06																						
118																											
119		SPECTROMETER MODIFICAITONS	48 days	Mon 7/24/06	Wed 9/27/06																						
120		Bring spectrometers down from the mountain	3 days	Mon 8/14/06	Wed 8/16/06																						
121		AOS OSCILLATOR MODIFICATION	48 days	Mon 7/24/06	Wed 9/27/06																						
122		7.1 GHz Oscillators (DRO)	45 days	Mon 7/24/06	Fri 9/22/06																						
123		Installation	3 days	Mon 9/25/06	Wed 9/27/06																						
124		Modify IF distribution to the FFB's	25 days	Mon 7/31/06	Fri 9/1/06																						
125		Order power splitters	20 days	Mon 7/31/06	Fri 8/25/06																						
126		Installation	5 days	Mon 8/28/06	Fri 9/1/06																						
127																											
128		SOFTWARE	10 days	Fri 9/22/06	Thu 10/5/06																						
129		Reassign bits from reallocating cards in card cage	2 days	Fri 9/22/06	Mon 9/25/06																						
130		Update the user interface screen	10 days	Fri 9/22/06	Thu 10/5/06																						
131																											
132		TEST RECEIVER	5 days	Fri 10/6/06	Thu 10/12/06																						
133																											
134		Isolation of the dewar electronics from the compressor	10 days	Fri 9/1/06	Thu 9/14/06																						
135		He line isolators	10 days	Fri 9/1/06	Thu 9/14/06																						
136		Fabricate	10 days	Fri 9/1/06	Thu 9/14/06																						
137		Isolation transformer for the compressor	6 days	Fri 9/1/06	Fri 9/8/06																						

Project: 1.3mm SSM RECEIVER UPG
Date: Fri 8/18/06

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

◊

Rolled Up Progress

Split

External Tasks

Project Summary

Group By Summary

Deadline

↓

Page 3
