



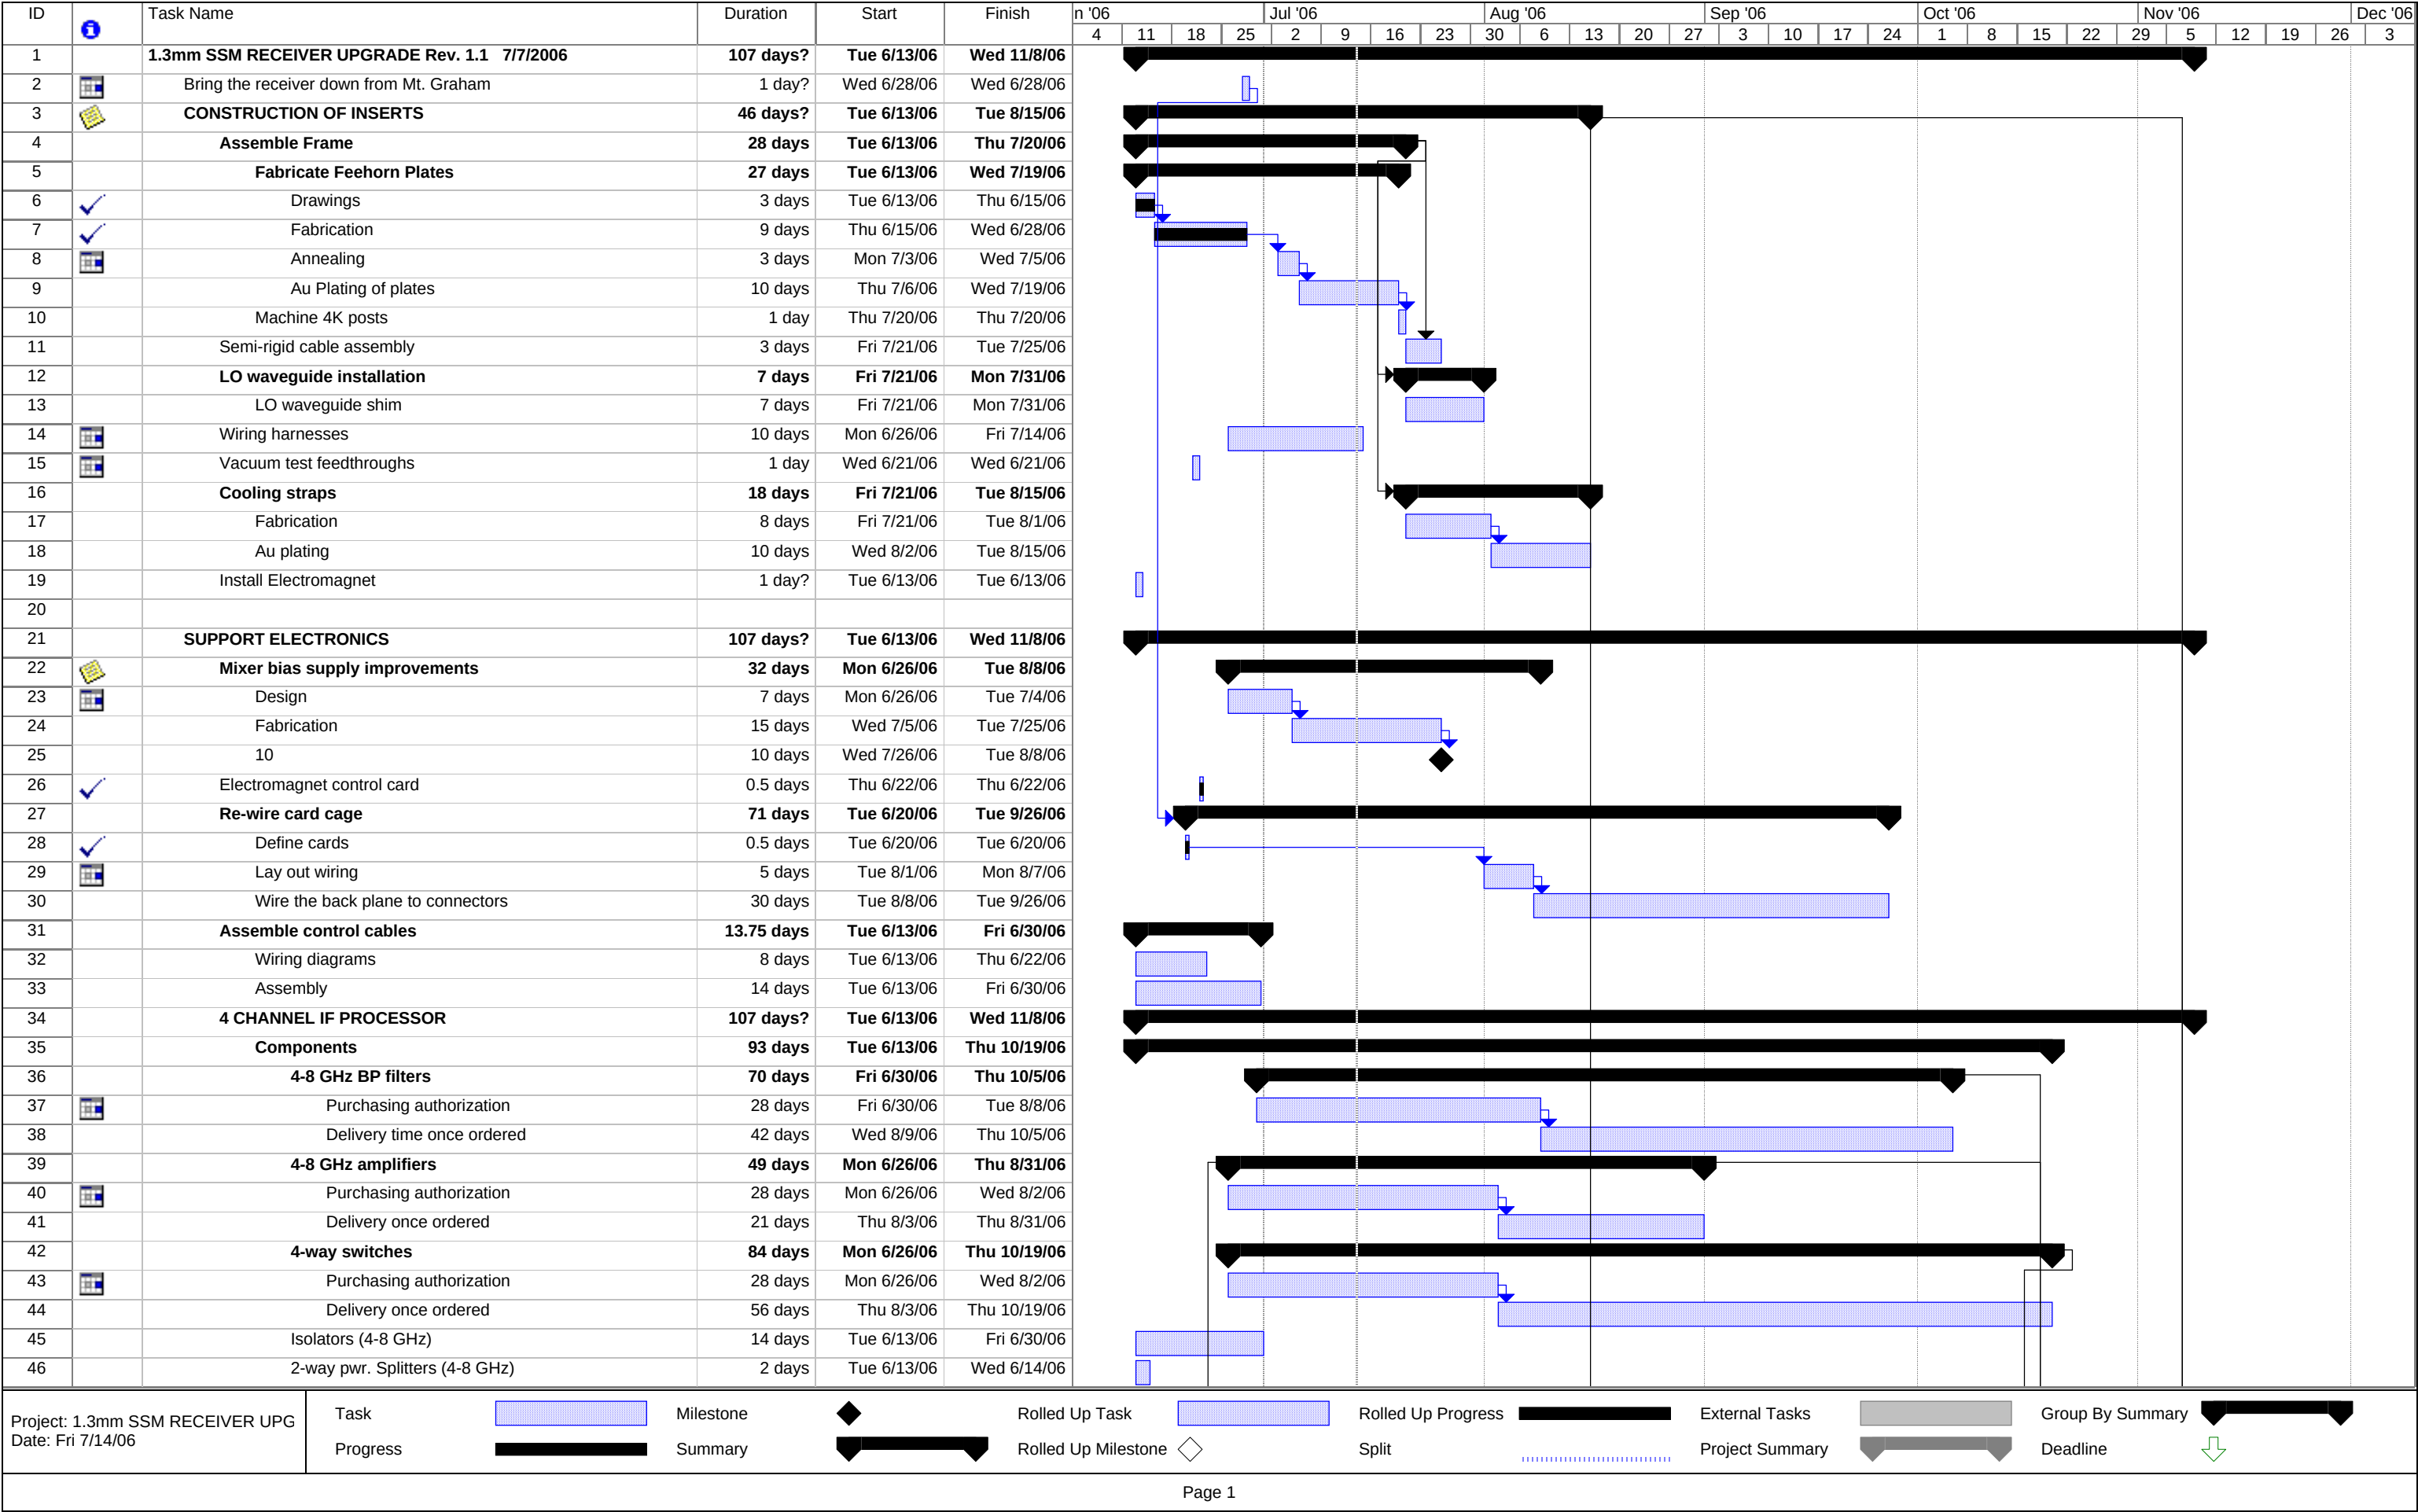

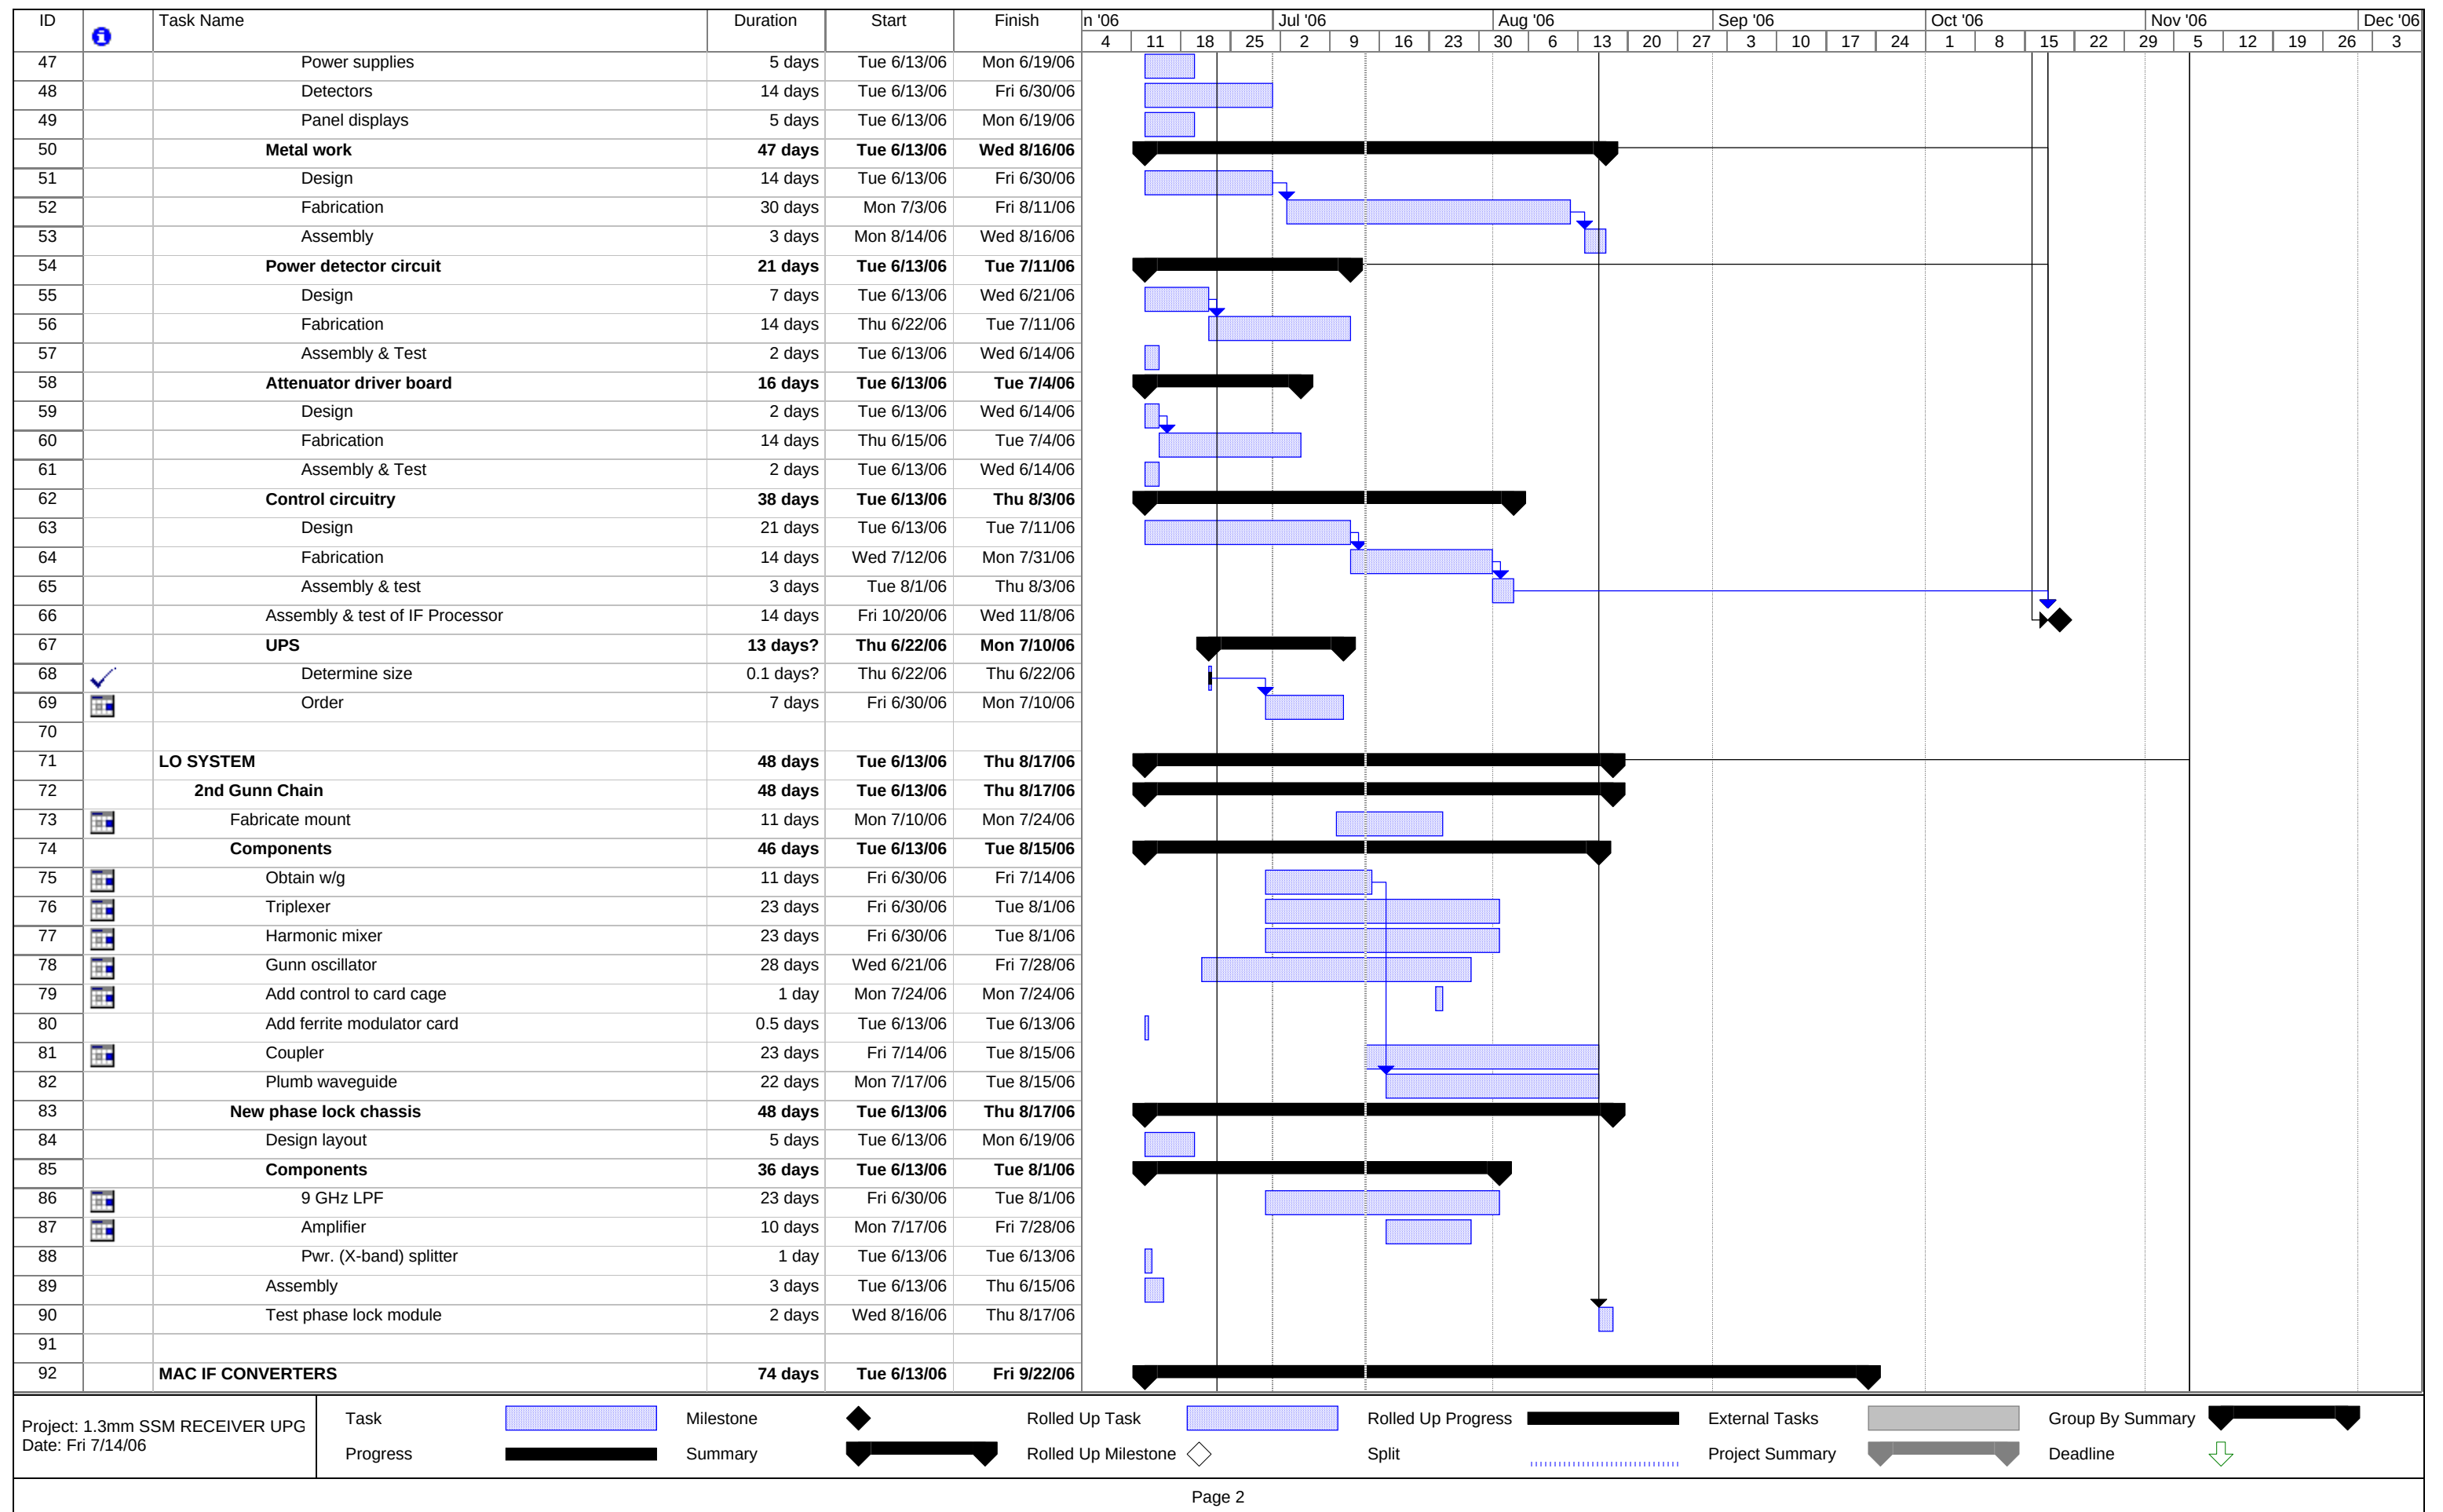

ID		Task Name	Duration	Start	Finish	n '06				Jul '06				Aug '06				Sep '06				Oct '06				Nov '06				Dec '06		
						4	11	18	25	2	9	16	23	30	6	13	20	27	3	10	17	24	1	8	15	22	29	5	12	19	26	3
93		Plan layout	3.5 days	Tue 6/13/06	Fri 6/16/06																											
94		Converter crate	25 days	Mon 7/10/06	Fri 8/11/06																											
95		Design	5 days	Mon 7/10/06	Fri 7/14/06																											
96		Fabrication	20 days	Mon 7/17/06	Fri 8/11/06																											
97		Power supply/LO box	23.5 days	Mon 7/10/06	Thu 8/10/06																											
98		Design	3.5 days	Mon 7/10/06	Thu 7/13/06																											
99		Fabrication	20 days	Thu 7/13/06	Thu 8/10/06																											
100		Components	57 days	Thu 7/6/06	Fri 9/22/06																											
101		4 - 8 GHz amplifiers	15 days	Wed 7/12/06	Tue 8/1/06																											
102		4 - 6 GHz output mixers	15 days	Wed 7/12/06	Tue 8/1/06																											
103		10. 4/1.3 GHz BPF's (Qty. 5)	57 days	Thu 7/6/06	Fri 9/22/06																											
104		Purchasing authorization	7 days	Thu 7/6/06	Fri 7/14/06																											
105		Delivery once ordered	50 days	Mon 7/17/06	Fri 9/22/06																											
106		Frequency control interface (Tuning box)	21 days	Thu 7/13/06	Thu 8/10/06																											
107																																
108		SOFTWARE	14 days	Thu 11/9/06	Tue 11/28/06																											
109		Reassign bits from reallocating cards in card cage	2 days	Thu 11/9/06	Fri 11/10/06																											
110		Update the user interface screen	14 days	Thu 11/9/06	Tue 11/28/06																											
111																																
112		TEST RECEIVER	5 days	Wed 11/29/06	Tue 12/5/06																											
113																																
114		Isolation of the dewar electronics from the compressor	10 days	Fri 9/1/06	Thu 9/14/06																											
115		He line isolators	10 days	Fri 9/1/06	Thu 9/14/06																											
116		Fabricate	10 days	Fri 9/1/06	Thu 9/14/06																											
117		Isolation transformer from the compressor	6 days	Fri 9/1/06	Fri 9/8/06																											
118																																
119		CHANNEL STEERING SELECTOR	20 days	Tue 9/5/06	Mon 10/2/06																											
120																																
121		AOS OSCILLATOR MODIFICATION	26 days	Fri 7/14/06	Fri 8/18/06																											
122		Order DRO's	25 days	Fri 7/14/06	Thu 8/17/06																											
123		Install	1 day	Fri 8/18/06	Fri 8/18/06																											
